


[illegible]

Page : 1 of 1

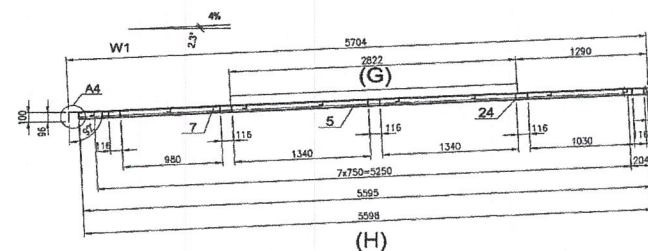

SEGMENT 1-2

A	B	C	D	E	F	G	H
1453	455	326	177	394	394	394	394
±10	±10	±10	±10	±10	±10	±10	±10
455	455	326	177	394	394	394	394

☐ REJECTED

PT. PLN (Persero) UIP NUSA TENGGARA

Gan Gan Dermawan


Gan Gan Dermawan

11. 11 20

DIMENSIONAL REPORT



Project : LOMBOK CFSPP FTP-2 (2X50MW)	Drawing No : LPP-239-MEC-VG-094-V	Report No. : LPP-239-MEC-DR-105-V
Client : PT.REKAYASA INDUSTRI	Item Name : C-160 / SEGMENT-2	Date : November 11, 2024
Job Code : E-2406	Item No. : 01, 02, 03, 04	Page : 1 of 2

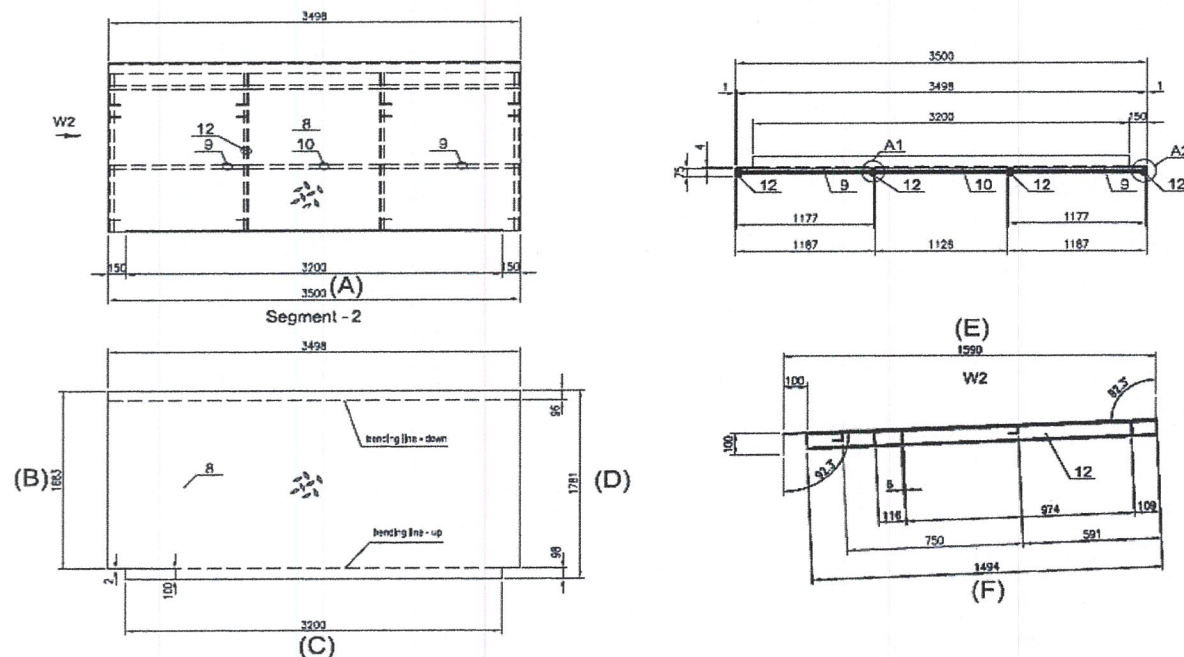

SEGMENT 2-1

Item Inspected	A	B	C	D	E	F
Design	3500	1683	3200	1781	1590	1494
Tolerance	±10	±10	±10	±10	±10	±10
Actual	3500	1683	3200	1781	1590	1494

SEGMENT 2-2

A	B	C	D	E	F
3500	1683	3200	1781	1590	1494
±10	±10	±10	±10	±10	±10
3500	1683	3200	1781	1590	1494

SEGMENT 2-3

A	B	C	D	E	F
3500	1683	3200	1781	1590	1494
±10	±10	±10	±10	±10	±10
3500	1683	3200	1781	1590	1494

SEGMENT 2-4

A	B	C	D	E	F
3500	1683	3200	1781	1590	1494
±10	±10	±10	±10	±10	±10
3500	1683	3200	1781	1590	1494

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By

Witnessed / Reviewed By

Witnessed / Reviewed By

Reviewed / Approved By

COMPANY

PT. HANAZONO ENGINEERING INDONESIA

PT. REKAYASA INDUSTRI

PT. PLN (Persero) UIP NUSA TENGGARA

Signature & Name

Benridho



Benridho

Rusnandi

Rusnandi

Gan Gan Dermawan

Gan Gan Dermawan

Date

Nov 11, 2024


11.11.2024

11.11.2024

DIMENSIONAL REPORT



Project : LOMBOK CFSPP FTP-2 (2X50MW)	Drawing No : LPP-239-MEC-VG-094-V	Report No. : LPP-239-MEC-DR-105-V
Client : PT.REKAYASA INDUSTRI	Item Name : C-160 / SEGMENT-2	Date : November 11, 2024
Job Code : E-2406	Item No. : 05, 06, 07, 08	Page : 2 of 2

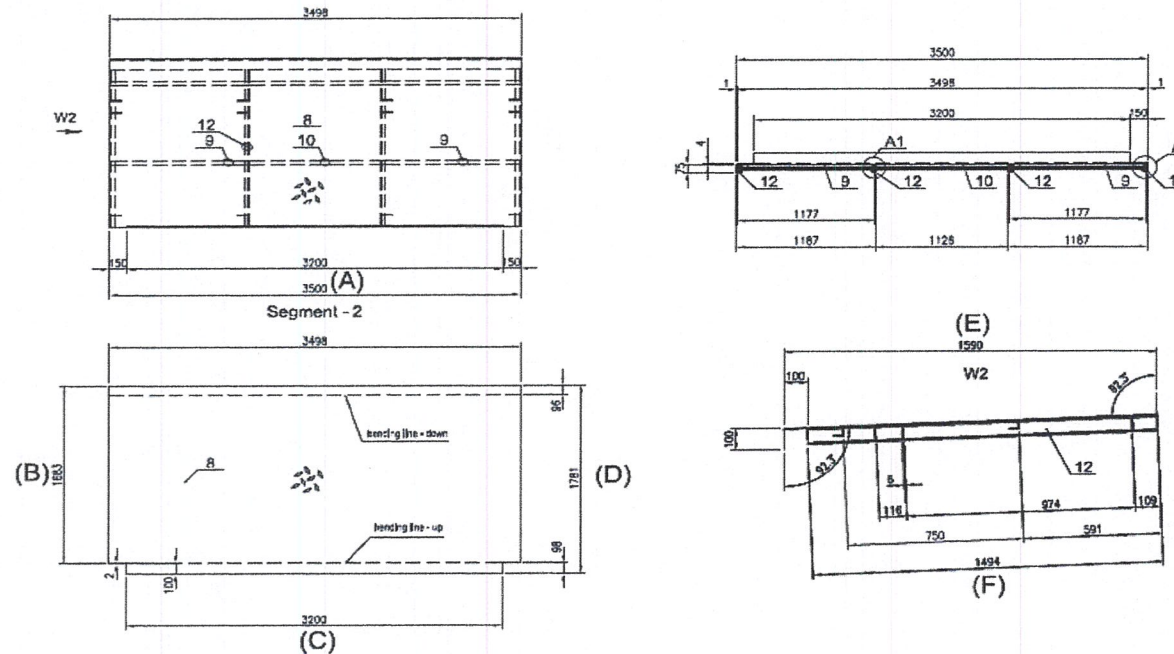

SEGMENT 2-5						
Item Inspected	A	B	C	D	E	F
Design	3500	1683	3200	1781	1590	1494
Tolerance	±10	±10	±10	±10	±10	±10
Actual	3500	1683	3200	1781	1590	1494

SEGMENT 2-6						
A	B	C	D	E	F	
3500	1683	3200	1781	1590	1494	
±10	±10	±10	±10	±10	±10	
3500	1683	3200	1781	1590	1494	

SEGMENT 2-7						
A	B	C	D	E	F	
3500	1683	3200	1781	1590	1494	
±10	±10	±10	±10	±10	±10	
3500	1683	3200	1781	1590	1494	

SEGMENT 2-8						
A	B	C	D	E	F	
3500	1683	3200	1781	1590	1494	
±10	±10	±10	±10	±10	±10	
3500	1683	3200	1781	1590	1494	

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By		Witnessed / Reviewed By	
COMPANY		PT. HANAZONO ENGINEERING INDONESIA	
Signature & Name		PT. REKAYASA INDUSTRI	
Date		Reviewed / Approved By	
Nov 11, 2024		PT. PLN (Persero) UIP NUSA TENGGARA	
Benridho		Gan Gan Dermawan	
Rusnandi		11-11-2024	

DIMENSIONAL REPORT



Project : LOMBOK CFSPF FTP-2 (2X50MW)

Client : PT.REKAYASA INDUSTRI

Job Code : E-2406

Drawing No : LPP-239-MEC-VG-095-V

Item Name : C-160 / SEGMENT-3



Item No. : 01, 02, 03, 04

Report No. : LPP-239-MEC-DR-106-V

Date : November 11, 2024

Page : 1 of 2

Segment - 3

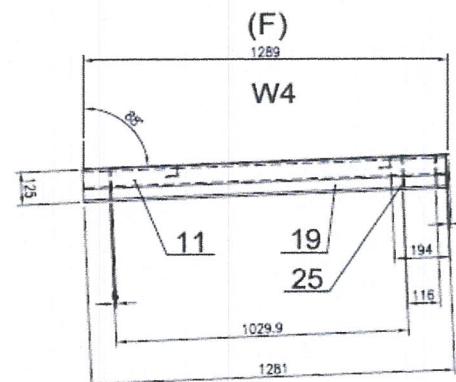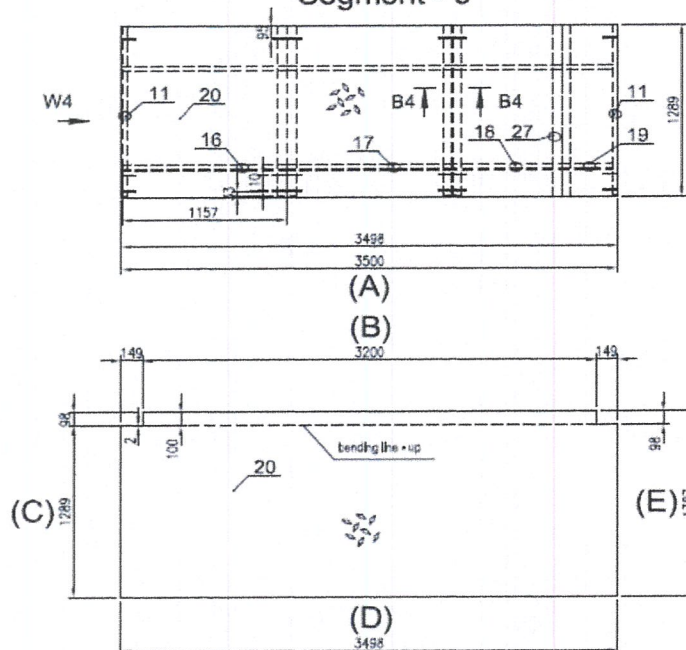

SEGMENT 3-1

Item Inspected	A	B	C	D	E	F
Design	3500	3200	1289	3498	1387	1289
Tolerance	±10	±10	±10	±10	±10	±10
Actual	3500	3200	1289	3498	1387	1289

SEGMENT 3-2

A	B	C	D	E	F
3500	3200	1289	3498	1387	1289
±10	±10	±10	±10	±10	±10
3500	3200	1289	3498	1387	1289

SEGMENT 3-3

A	B	C	D	E	F
3500	3200	1289	3498	1387	1289
±10	±10	±10	±10	±10	±10
3500	3200	1289	3498	1387	1289

SEGMENT 3-4

A	B	C	D	E	F
3500	3200	1289	3498	1387	1289
±10	±10	±10	±10	±10	±10
3500	3200	1289	3498	1387	1289

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By

Witnessed / Reviewed By

Witnessed / Reviewed By

Reviewed / Approved By

COMPANY

PT. HANAZONO ENGINEERING INDONESIA

PT. REKAYASA INDUSTRI

PT. PLN (Persero) UIP NUSA TENGGARA

Signature & Name

Benridho

Benridho



Rusnandi

Gan Gan Dermawan

Gan Gan Dermawan

Date

Nov 11, 2024

Nov 11, 2024


Nov 11, 2024

11. 11.2er

DIMENSIONAL REPORT



Project : LOMBOK CFSPF FTP-2 (2X50MW)	Drawing No : LPP-239-MEC-VG-095-V	Report No. : LPP-239-MEC-DR-107-V
Client : PT.REKAYASA INDUSTRI	Item Name : C-160 / SEGMENT-4	Date : November 11, 2024
Job Code : E-2406	Item No. : 01, 02	Page : 1 of 1

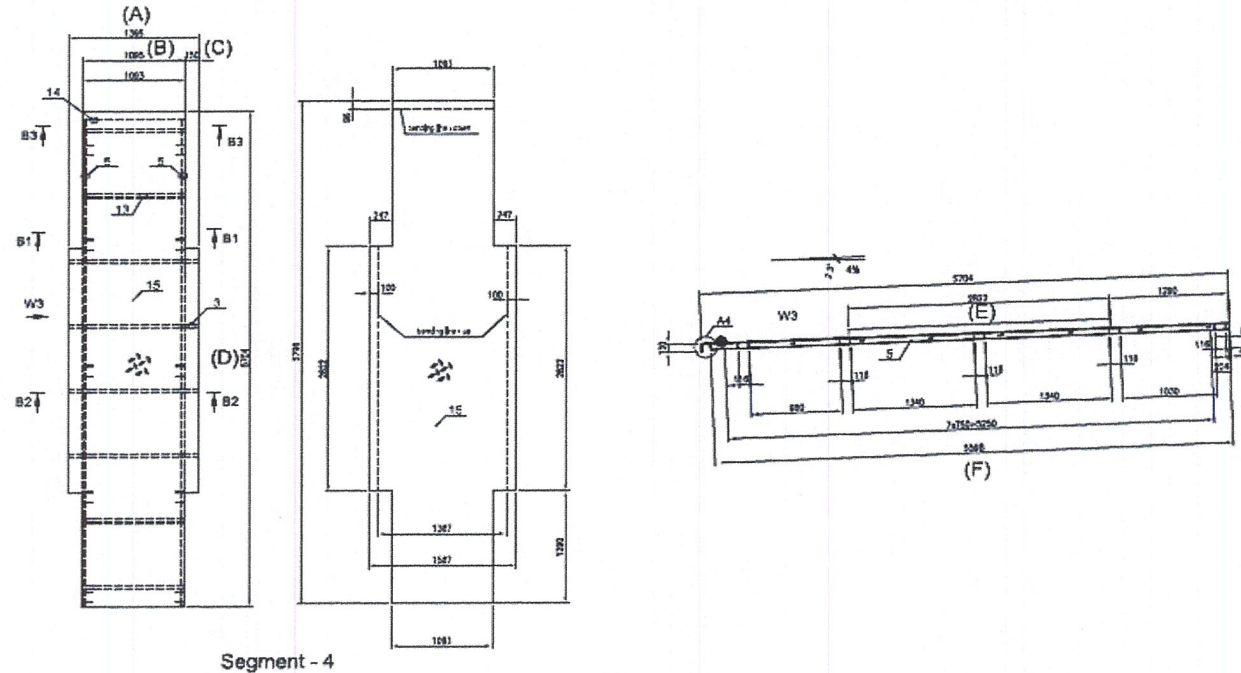

SEGMENT 4-1

Item Inspected	A	B	C	D	E	F
Design	1395	1095	150	5704	2822	5598
Tolerance	±10	±10	±10	±10	±10	±10
Actual	1395	1095	150	5704	2822	5598

SEGMENT 4-2

A	B	C	D	E	F
1395	1095	150	5704	2822	5598
±10	±10	±10	±10	±10	±10
1395	1095	150	5704	2822	5598

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By

Witnessed / Reviewed By

Witnessed / Reviewed By

Reviewed / Approved By

COMPANY

PT. HANAZONO ENGINEERING INDONESIA

PT. REKAYASA INDUSTRI

PT. PLN (Persero) UIP NUSA TENGGARA

Signature & Name

Benridho

Benridho



Rusnandi

Gan Gan Dermawan

Gan Gan Dermawan

Date

NOV 11, 2024

NOV 11, 2024

11-11-24

DIMENSIONAL REPORT



Project : LOMBOK CFSPP FTP-2 (2X50MW)

Client : PT.REKAYASA INDUSTRI

Job Code : E-2406

Drawing No : LPP-239-MEC-VG-096-V


Item Name : C-160 / SEGMENT-5

Item No. : 01, 02, 03, 04

Report No. : LPP-239-MEC-DR-108-V

Date : November 11, 2024

Page : 1 of 1

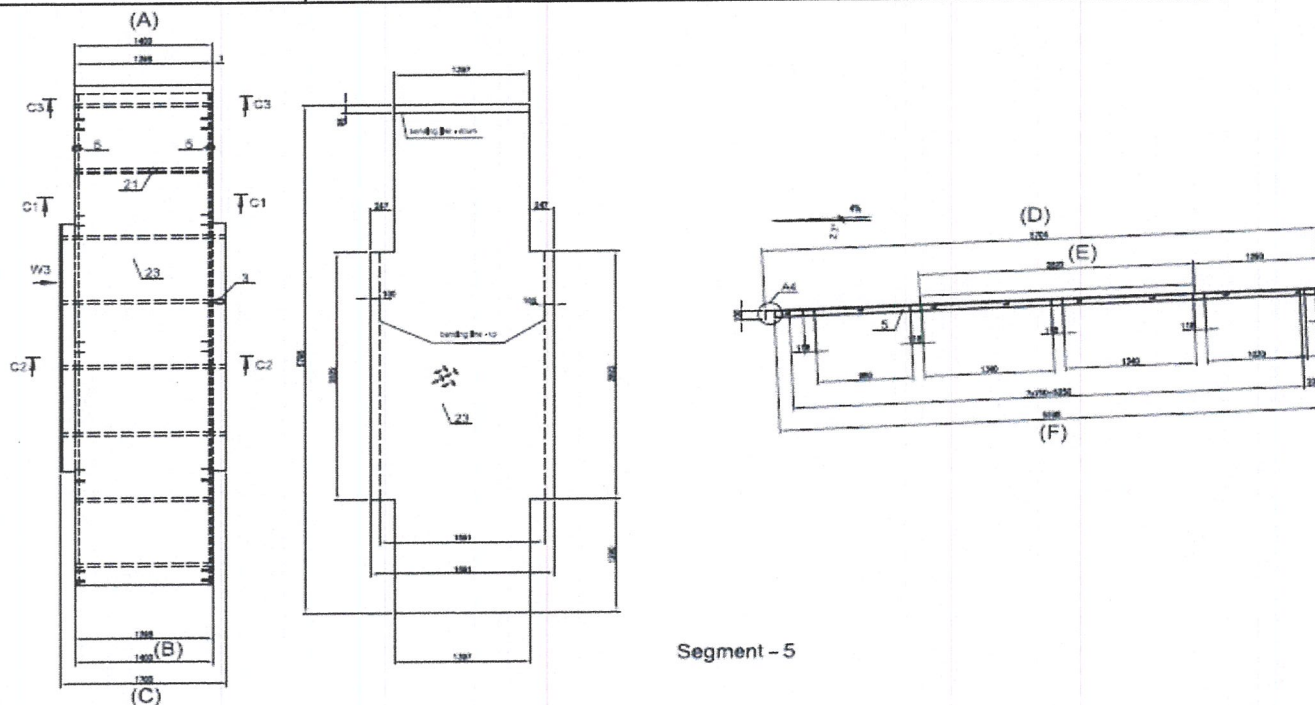

SEGMENT 5-1

Item Inspected	A	B	C	D	E	F
Design	1400	1400	1700	5704	2822	5598
Tolerance	±10	±10	±10	±10	±10	±10
Actual	1400	1400	1700	5704	2822	5598

SEGMENT 5-2

A	B	C	D	E	F
1400	1400	1700	5704	2822	5598
±10	±10	±10	±10	±10	±10
1400	1400	1700	5704	2822	5598

SEGMENT 5-3

A	B	C	D	E	F
1400	1400	1700	5704	2822	5598
±10	±10	±10	±10	±10	±10
1400	1400	1700	5704	2822	5598

SEGMENT 5-4

A	B	C	D	E	F
1400	1400	1700	5704	2822	5598
±10	±10	±10	±10	±10	±10
1400	1400	1700	5704	2822	5598

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By

Witnessed / Reviewed By

Witnessed / Reviewed By

Reviewed / Approved By

COMPANY

PT. HANAZONO ENGINEERING INDONESIA

PT. REKAYASA INDUSTRI

PT. PLN (Persero) UIP NUSA TENGGARA

Signature & Name

Benridho

Benridho



Rusnandi

Gan Gan Dermawan

Gan Gan Dermawan

Date

Nov 11, 2024

11.11.24

Project : LOMBOK CFSPP FTP-2 (2X50MW)

Drawing No : LPP-239-MEC-VG-097-V

Report No. : LPP-239-MEC-DR-109-V

Client : PT.REKAYASA INDUSTRI



Item Name : C-160 / SEGMENT-6

Date : November 11, 2024

Job Code : E-2406

Item No. : 01, 02

Page : 1 of 1

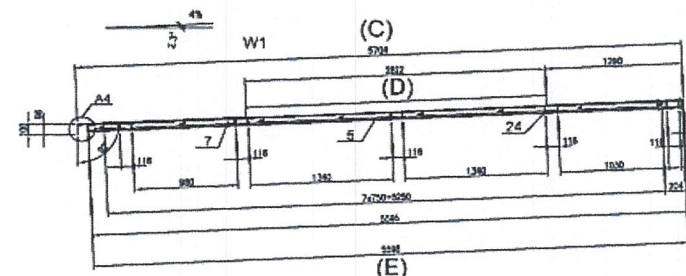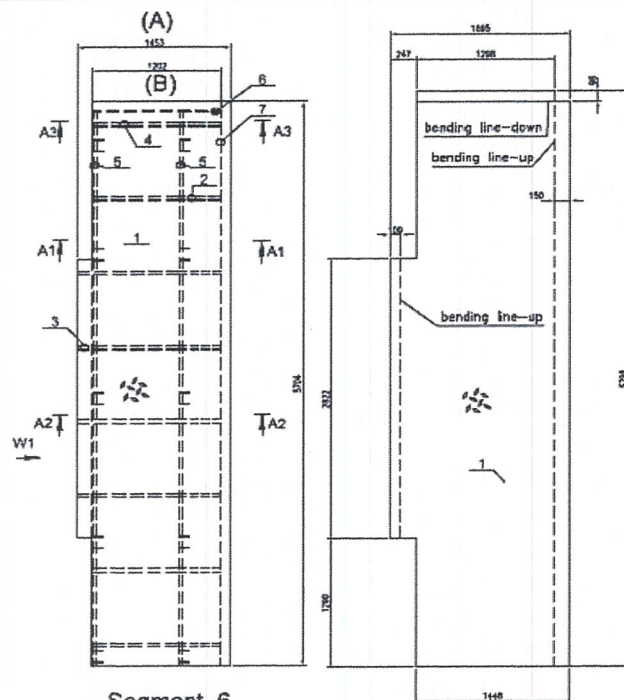

Segment -6

SEGMENT 6-1

SEGMENT 6-2

Item Inspected	A	B	C	D	E
Design	1453	1202	5704	2822	5598
Tolerance	±10	±10	±10	±10	±10
Actual	1453	1202	5704	2822	5598

A	B	C	D	E
1453	1202	5704	2822	5598
±10	±10	±10	±10	±10
1453	1202	5704	2822	5598

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By

Witnessed / Reviewed By

Witnessed / Reviewed By

Reviewed / Approved By

COMPANY

PT. HANAZONO ENGINEERING INDONESIA

PT. REKAYASA INDUSTRI

PT. PLN (Persero) UIP NUSA TENGGARA


Signature & Name



Benridho



Rusnandi



Gan Gan Dermawan

Date

Nov 11, 2024

Nov 11, 2024

11 - 11 - 24
