

[illegible]


DIMENSIONAL REPORT



Project : LOMBOK CFSPP FTP-2 (2X50MW)
Client : PT.REKAYASA INDUSTRI
Job Code : E-2406

Drawing No : LPP-239-MEC-VG-142-V
Item Name : C-410 Gas Distribution Device In Diffuser
Item No. : Devices 1

Report No. : LPP-239-MEC-DR-114-V
Date : December 11, 2024
Page : 1 of 1

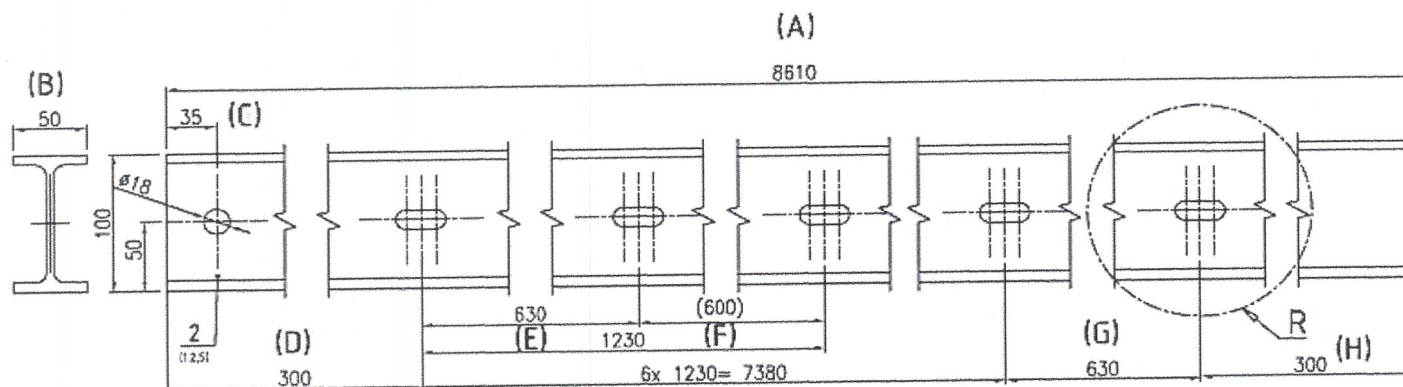

DEVICES-1

Item Inspected	A	B	C	D	E	F	G	H
Design	8610	50	35	300	630	600	630	300
Tolerance	±10	±10	±10	±10	±10	±10	±10	±10
Actual	8610	50	35	300	630	600	630	300

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By

Witnessed / Reviewed By

Witnessed / Reviewed By

Reviewed / Approved By

COMPANY

PT. HANAZONO ENGINEERING INDONESIA

PT. REKAYASA INDUSTRI

PT. PLN (Persero) UIP NUSA TENGGARA

Signature & Name

Benridho

Benridho



Rusnandi

Rusnandi

Gan/Gan Dermawan

Gan/Gan Dermawan

Date

12-12-2024


Dec 12. 2024

Dec. 12. 2024

DIMENSIONAL REPORT



Project : LOMBOK CFSPP FTP-2 (2X50MW)	Drawing No : LPP-239-MEC-VG-143-V	Report No. : LPP-239-MEC-DR-115-V
Client : PT.REKAYASA INDUSTRI	Item Name : C-410 Gas Distribution Device In Diffuser	Date : December 11, 2024
Job Code : E-2406	Item No. : Devices 2	Page : 1 of 1

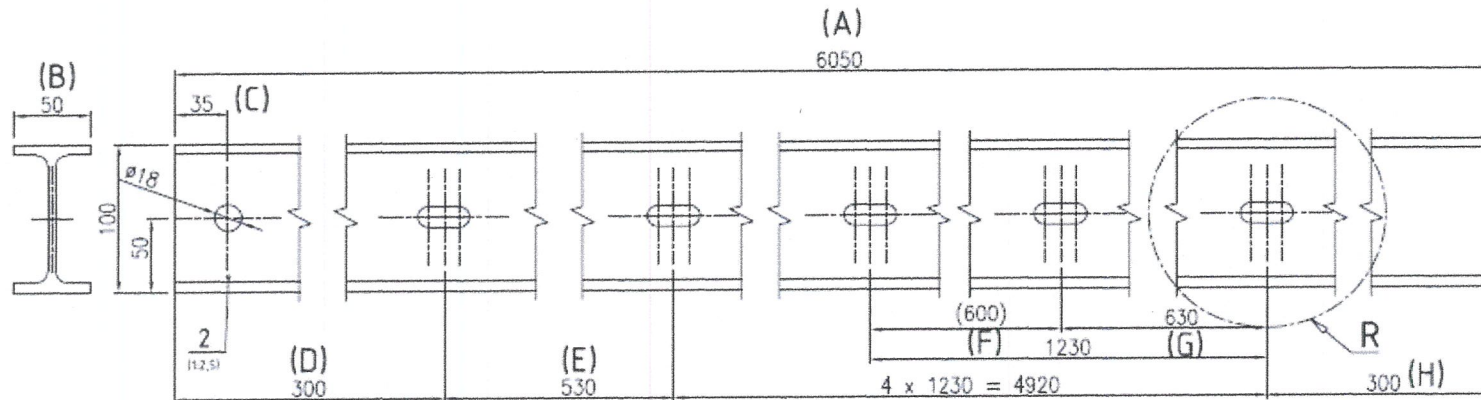

DEVICES-1

Item Inspected	A	B	C	D	E	F	G	H
Design	6050	50	35	300	530	600	630	300
Tolerance	±10	±10	±10	±10	±10	±10	±10	±10
Actual	6050	50	35	300	530	600	630	300

RESULT OF INSPECTION

☒ ACCEPTED


☐ REJECTED

COMPANY	Inspected By	Witnessed / Reviewed By	Witnessed / Reviewed By	Reviewed / Approved By
	PT. HANAZONO ENGINEERING INDONESIA		PT. REKAYASA INDUSTRI	PT. PLN (Persero) UIP NUSA TENGGARA
Signature & Name	 Benridho	 Rusnandi	 Gan Gan Dermawan	
Date	12-12-2024	Dec 12, 2024	Dec 12, 2024	

DIMENSIONAL REPORT



Project : LOMBOK CFSPF FTP-2 (2X50MW)	Drawing No : LPP-239-MEC-VG-144-V	Report No. : LPP-239-MEC-DR-116-V
Client : PT.REKAYASA INDUSTRI	Item Name : C-410 Gas Distribution Device In Diffuser	Date : December 11, 2024
Job Code : E-2406	Item No. : Stator Blade	Page : 1 of 1

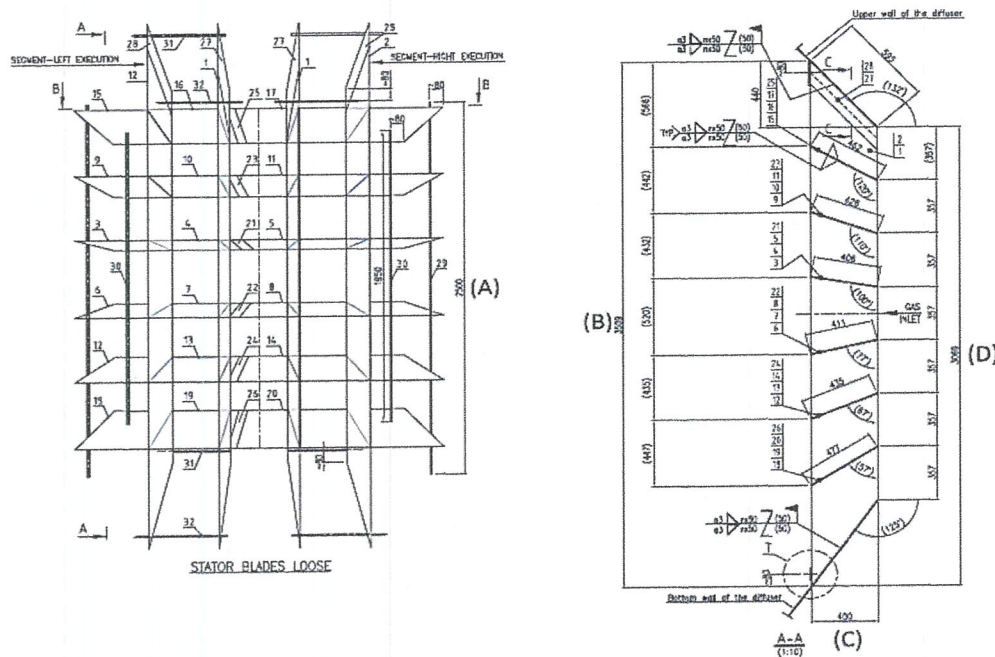

STATOR BLADE

Item Inspected	A	B	C	D
Design	2500	3509	400	3069
Tolerance	±10	±10	±10	±10
Actual	2500	3509	400	3069

RESULT OF INSPECTION

☒ ACCEPTED



☐ REJECTED

COMPANY	Inspected By	Witnessed / Reviewed By	Witnessed / Reviewed By	Reviewed / Approved By
	PT. HANAZONO ENGINEERING INDONESIA		PT. REKAYASA INDUSTRI	PT. PLN (Persero) UIP NUSA TENGGARA
Signature & Name	 Benridho	 Rusnandi	 Gan Gan Dermawan	
Date	12-12-24	Dec 12. 2024	Dec. 12. 2024	

DIMENSIONAL REPORT



Project : LOMBOK CFSPF FTP-2 (2X50MW)	Drawing No : LPP-239-MEC-VG-141-V	Report No. : LPP-239-MEC-DR-117-V
Client : PT.REKAYASA INDUSTRI	Item Name : C-410 Gas Distribution Device In Diffuser	Date : December 11, 2024
Job Code : E-2406	Item No. : Panel	Page : 1 of 1

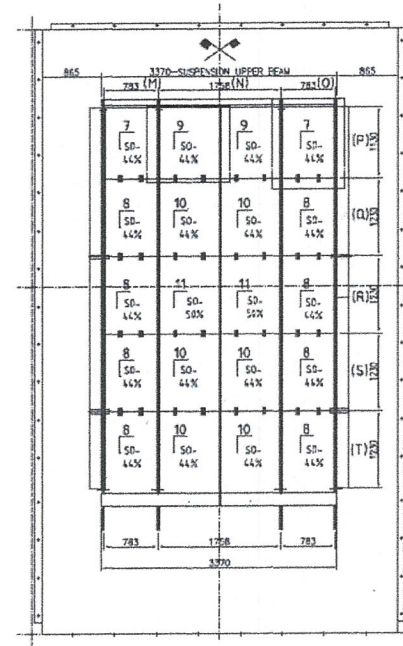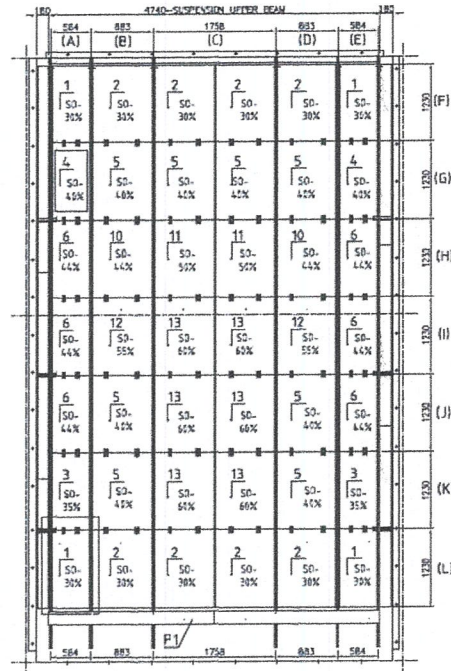

PANEL SO

Item Inspected	A	B	C	D	E	F	G	H	I	J	K	L	M	N	O	P	Q	R	S	T
Design	584	883	1758	883	584	1230	1230	1230	1230	1230	1230	1230	783	1758	783	1130	1230	1230	1230	1230
Tolerance	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10	±10
Actual	584	883	1758	883	584	1230	1230	1230	1230	1230	1230	1230	783	1758	783	1130	1230	1230	1230	1230

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

Inspected By	Witnessed / Reviewed By	Witnessed / Reviewed By	Reviewed / Approved By
COMPANY	PT. HANAZONO ENGINEERING INDONESIA	PT. REKAYASA INDUSTRI	PT. PLN (Persero) UIP NUSA TENGGARA
Signature & Name	Benridho Rusnandi	Gan Gan Dermawan	
Date	12-12-2024	Dec. 12. 2024	
