


LOMBOK CFSPP FTP-2 (2X50 MW) PROJECT CONTRACTOR DOCUMENT REVIEW		Review	Discipline	Sign	
			Civil		
			Mechanical		
			Electrical		
			I & C		
Log In	Date : Comm. No :		Support		
A	☐ Approved	Distribution	Contractor Record		
B	☐ Approved as Note		Working Document		
C	☐ Not Approved				
I	☐ Information				
APPROVAL DOES NOT RELIEVE CONTRACTOR FROM RESPONSIBILITY FOR ERRORS AND DEVIATIONS FROM CONTRACT REQUIREMENT					
By :	Date :				
Log Out	Date : Comm. No :				
Owner :			PT. PERUSAHAAN LISTRIK NEGARA (PERSERO) UNIT INDUK PEMBANGUNAN NUSA TENGGARA		
Engineer :			PT. PERUSAHAAN LISTRIK NEGARA (PERSERO) PUSAT ENJINIRING KETENAGALISTRIKAN		
Contract No :					
PLN Doc No :					
Title :		DIMENSIONAL INSPECTION REPORT FOR AREA C420			
Purpose :		ISSUE FOR APPROVAL			
Rev	Description	Prepared	Checked	Approved	Date
0	For Approval	Benridho	Rusnandi	Musato	17-April-2025
 PT. HANAZONO ENGINEERING INDONESIA		ITEM NO			
		EQUIPMENT NAME		ESP PLATWORK FOR BOILER UNIT 2	
		PO.NO		LPP-10-F9-PO-239-R	
Contractor :		Consortium Of		Doc. No :	
 Rekind Integrated EPC and Industrial Solutions RAFAKO GRUPA PBG				LPP-239-MEC-VS-285-V	

Page : 1 of 1



Item Inspected	A	B	C
Design	246	700	4775
Tolerance	± 10	± 10	± 10
Actual	246	700	4775

Gan Gan Dermawan

Date _____


DIMENSIONAL REPORT



Project : LOMBOK CFSPP FTP-2 (2X50MW)
Client : PT.REKAYASA INDUSTRI
Job Code : E-2406

Drawing No : LPP-239-MEC-VG-151-V
Item Name : C-420 Gas Distribution Device In Confuser
Item No. : Upper Suspension Beam

Report No. : LPP-239-MEC-DR-120-V
Date : December 11, 2024
Page : 1 of 1

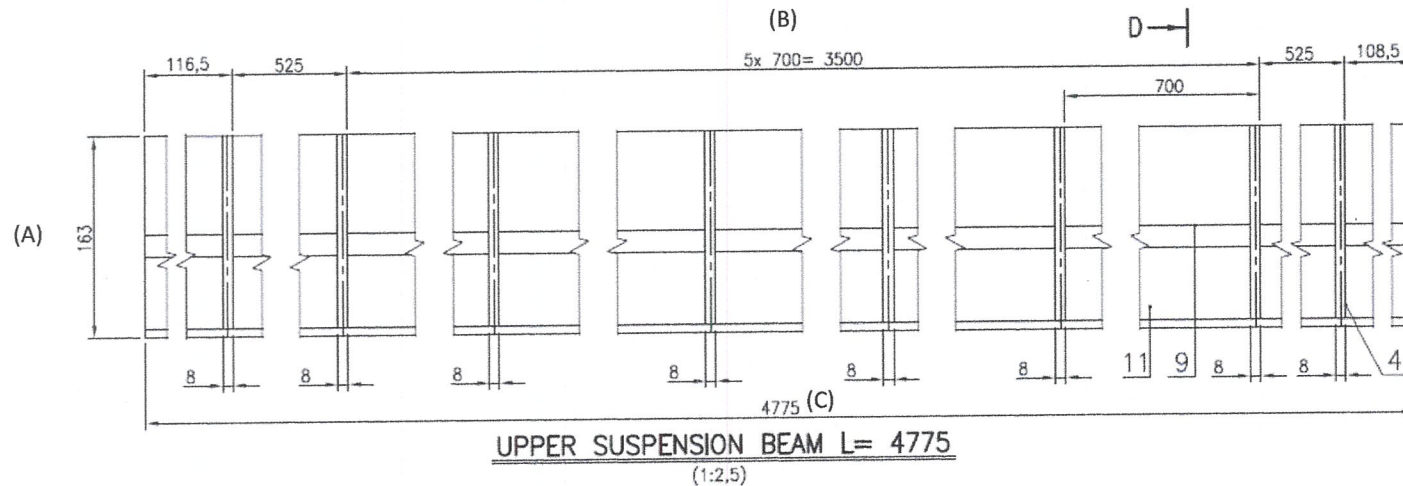



Upper Suspension

Item Inspected	A	B	C
Design	163	700	4775
Tolerance	±10	±10	±10
Actual	163	700	4775

RESULT OF INSPECTION

☒ ACCEPTED

☐ REJECTED

COMPANY	Inspected By	Witnessed / Reviewed By	Witnessed / Reviewed By	Reviewed / Approved By
	PT. HANAZONO ENGINEERING INDONESIA		PT. REKAYASA INDUSTRI	PT. PLN (Persero) UIP NUSA TENGGARA
Signature & Name	 Benridho	 Rusnandi	 Gan Gan Dermawan	
Date		Dec 11, 2024	Dec 11, 2024	
